





FAST DANUBE 2

Improvement of Navigation Conditions on the Romanian-Bulgarian Common Sector of the Danube

Co-financed by the European Union
Connecting Europe Facility

FAST DANUBE 2
Implementation Strategy

2nd Steering Committee Meeting

10.12.2025, Bucharest

FAST DANUBE 2

The FAST DANUBE 2 project involves the following activities:

- Organizing the Joint procurement procedure and signing the Environmental Monitoring Contract
- Organizing the Joint procurement procedure and signing the Design & Execution of Works Contract
- Organizing the Joint procurement procedure and signing the Design & Execution of Works Contract
- Detailed technical design development
- Execution of works
- Monitoring the impact of works on the environment
- Supervision and management of the execution of works





Co-financed by the European Union
Connecting Europe Facility

FAST DANUBE 2

Preliminary activities :

- Signing Agreements for joint procurements;
- Carrying out the procedure for approving technical and economic indicators:
  - ✓ Approval by the CTE AFDJ – July 2025;
  - ✓ Approval in the MTI CTE – July 2025;
  - ✓ Approval in the Interministerial Committee – August 2025
  - ✓ Issuance of a Government Decision – December 2025.





Co-financed by the European Union
Connecting Europe Facility

FAST DANUBE 2

The FAST DANUBE 2 project involves the following activities:

- ***Organizing the Joint procurement procedure and signing the Environmental Monitoring Contract***

The procurement procedure will be carried out by AFDJ, as the procurement leader.

The Agreement for joint procurement was signed by both project partners in 24.04.2025.





Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

- ***Organizing the Joint procurement procedure and signing the Environmental Monitoring Contract***

	Procedure step	To-Do	Deadline
Preparation	Draft tender documentation	– Draft tender documentation completion – Submission of the tender documentation to EAEMDR – Incorporation the recommendations; – Draft tender documentation ready for submission to the Technical and Economical Committee of AFDJ for approval	July 2025





Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

- ***Organizing the Joint procurement procedure and signing the Environmental Monitoring Contract***

	Procedure step	To-Do	Deadline
Tender procedure	Tender notice	– Aproval by CTE AFDJ documentation for publication – Send the tender documentation for publication on RO SICAP and EUOJ (ted.europa.eu) – Publication of the participation notice on SICAP and EUOJ	September 2025
	Evaluation of best bidder	– Offers opening – Evaluation of the offers – Request missing documents and clarification from bidders – Draft assessment report – Submission of the assessment to EAEMDR – Draft award proposal – Send award notice to all bidder	February 2026

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline - Procurement for environmental monitoring

- ***Organizing the Joint procurement procedure and signing the Environmental Monitoring Contract***

	Procedure step	To-Do	Deadline
Contract signature	Award of contract	– After expiration of 10 days challenge period: award of contract – Contract signature – Publication the award notice on EUOJ	February 2026

Contract duration - 108 months (March 2026 - February 2035)
In accordance with the environmental permits issued in Romania and Republic of Bulgaria, the environmental monitoring program will be carried out 9 years (108 months)

- 2 years before the start of the works *(03/2026 – 02/2028),*
- 2 years during the execution of the works *(03/2028 – 02/2030)*
- 5 years after the completion of the works, as follows:
  - *3 years for all environmental factors (03/2030 – 02/2033)*
  - and further *2 years of monitoring only for biodiversity factors (03/2033 – 02/2035)*

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢ ***Organizing the Joint procurement procedure and signing the Design & Execution of Works Contract***

The procurement procedure will be carried out by AFDJ, as the procurement leader.

The Agreement for joint procurement was signed by both project partners in 22.07.2025.

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢ ***Organizing the Joint procurement procedure and signing the Design & Execution of Works Contract***

	Procedure step	To-Do	Deadline
Preparation	Draft tender documentation	– Draft tender documentation completion – Submission of the tender documentation to EAEMDR – Incorporation the recommendations; – Draft tender documentation ready for submission to the Technical and Economical Committee of AFDJ for approval	September 2025





Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢ ***Organizing the Joint procurement procedure and signing the Design & Execution of Works Contract***

	Procedure step	To-Do	Deadline
Tender procedure	Tender notice	– Aproval by CTE AFDJ documentation for publication – Send the tender documentation for publication on RO SICAP and EUOJ (ted.europa.eu) – Publication of the participation notice on SICAP and EUOJ – Offers opening	February 2026
	Evaluation of best bidder	– Evaluation of the offers – Request missing documents and clarification from bidders – Draft assessment report – Submission of the assessment to EAEMDR – Draft award proposal – Send award notice to all bidder	October 2026

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢ ***Organizing the Joint procurement procedure and signing the Design & Execution of Works Contract***

	Procedure step	To-Do	Deadline
Contract signature	Award of contract	– After expiration of 10 days challenge period: award of contract – Contract signature – Publication the award notice on EUOJ	October 2026

Contract duration – 108 months (October 2026 – September 2035):

- Design stage, including construction permits issuance – 17 months (10.2026 –02.2028);
- Work execution stage – 24 months (03.2028 – 12.2029)
- Post – execution stage (warranty period) – 60 months (01.2030 – 12.2034)

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢***Organizing the Joint procurement procedure and signing the Supervision of the Works Execution Contract***

The procurement procedure will be carried out by AFDJ, as the procurement leader.

The Agreement for joint procurement was signed by both project partners in 22.07.2025.

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢ ***Organizing the Joint procurement procedure and signing the Supervision of the Works Execution Contract***

	Procedure step	To-Do	Deadline
Preparation	Draft tender documentation	– Draft tender documentation completion – Submission of the tender documentation to EAEMDR – Incorporation the recommendations; – Draft tender documentation ready for submission to the Technical and Economical Committee of AFDJ for approval – Aproval by CTE AFDJ documentation for publication	December 2025





Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢ ***Organizing the Joint procurement procedure and signing the Supervision of the Works Execution Contract***

	Procedure step	To-Do	Deadline
Tender procedure	Tender notice	– Send the tender documentation for publication on RO SICAP and EUOJ (ted.europa.eu) – Publication of the participation notice on SICAP and EUOJ – Offers opening	December 2025
	Evaluation of best bidder	– Evaluation of the offers – Request missing documents and clarification from bidders – Draft assessment report – Submission of the assessment to EAEMDR – Draft award proposal – Send award notice to all bidder	May 2026

Co-financed by the European Union
Connecting Europe Facility

Overview Timeline – Procurement for environmental monitoring

➢ ***Organizing the Joint procurement procedure and signing the Supervision of the Works Execution Contract***


	Procedure step	To-Do	Deadline
Contract signature	Award of contract	– After expiration of 10 days challenge period: award of contract – Contract signature – Publication the award notice on EUOJ	May 2026

Contract duration – 110 months since the Starting Order (May 2026 – November 2035)

The contract for supervision has a duration of 2 months longer compared to the duration of the design and works contract, needed for the elaboration of the final report, after the end of the warranty of the works period.

Co-financed by the European Union
Connecting Europe Facility



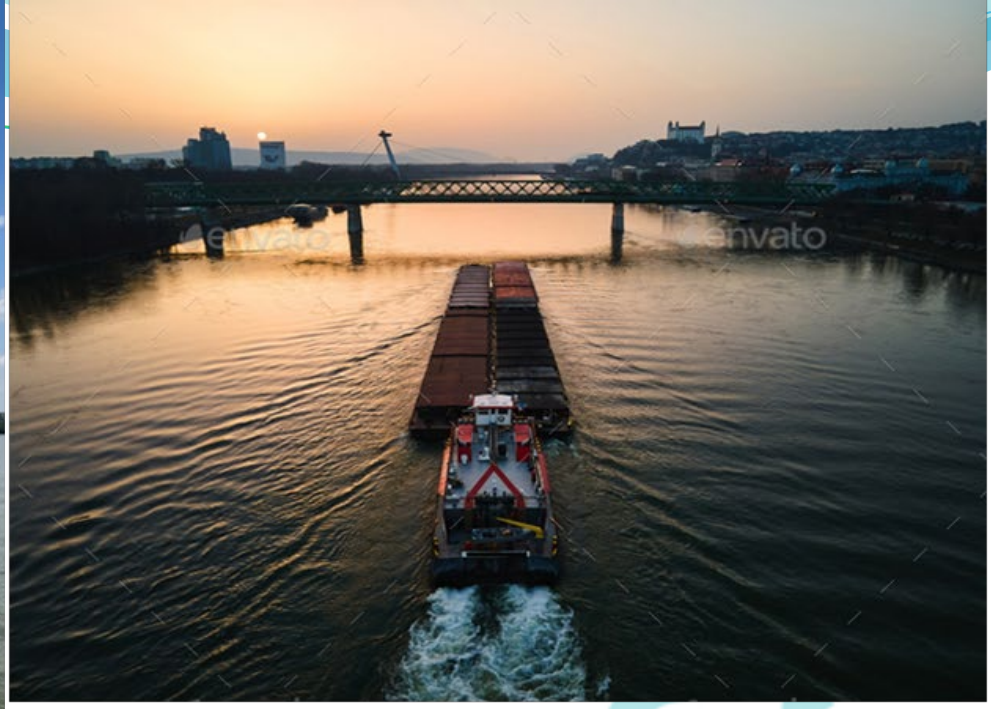

Thank you for your attention!

AFDJ Galati Team

IAPPD Ruse Team

EAEMDR Ruse

Co-financed by the European Union
Connecting Europe Facility
